

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	10 Mar '25 17 Mar '25 S M T W T F S S M T W T F													
1			Preparation	8 days	Mon 10.3.25	Wed 19.3.25																
2			Založiť GitHub repozitár			Tue 18.3.25		Lukáš Úradník														
3			Odtestovať validitu CSharpMath pre grafické rozhranie			Tue 18.3.25		Roman Láncoš														
4			Založiť Discord server na tímovu komunikáciu	1 day	Mon 10.3.25	Mon 10.3.25		Katarína Kužmová														
5			Nainštalovať MS Project	1 day	Wed 19.3.25	Wed 19.3.25		Katarína Kužmová; Lukáš Úradník; Roman Láncoš														
6			Project setup	3 days	Fri 21.3.25	Tue 25.3.25	1															
7			Vytvoriť podklad projektov vo Visual Studio Solution-e	1 day	Mon 24.3.25	Mon 24.3.25	8;9;10;11	Lukáš Úradník														
8			Windows Form projekt	1 day	Fri 21.3.25	Fri 21.3.25																
9			Matematická knižnica	1 day	Fri 21.3.25	Fri 21.3.25																

Project: xuradnl00_xkuzmok00_

Date: Wed 19.3.25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	S 10 Mar '25 M T W T F S S 17 Mar '25 M T W T F
18			Implementacia zadavania vyrokov	7 days	Thu 27.3.25	Fri 4.4.25	15	Roman Láncoš	
19			Transformator LaTeX -> MAT	3 days	Mon 7.4.25	Wed 9.4.25	18	Lukáš Úradník	
20	 		Rekurzívne vyhodnotenie príkladu	5 days	Thu 10.4.25	Wed 16.4.25	21;19	Katarína Kužmová; Lukáš Úradník	
21			Testy na vyhodnotenie vyrokov	3 days	Mon 7.4.25	Wed 9.4.25	17	Katarína Kužmová	
22			Testy UI zadavanie	4 days	Mon 7.4.25	Thu 10.4.25	18	Lukáš Úradník; Roman	
23			Testovanie celkovej kalkulacky	3 days	Thu 17.4.25	Mon 21.4.25	18;19;20	Lukáš Úradník	
24			Profilling	2 days	Mon 7.4.25	Tue 8.4.25	17	Lukáš Úradník	
25			Doplňkové úlohy	14 days	Mon 7.4.25	Thu 24.4.25			
26			Dokumentacia - MAT	2 days	Thu 17.4.25	Fri 18.4.25	20	Katarína Kužmová	
27			Dokumentacia - WF	2 days	Mon 7.4.25	Tue 8.4.25	18	Roman Láncoš	
28			Návrh Mockupu	1 day	Tue 22.4.25	Tue 22.4.25	23	Katarína Kužmová	
29			implementacia dizajnu Mockupu	1 day	Wed 23.4.25	Wed 23.4.25	28	Roman Láncoš	

Project: xuradnl00_xkuzmok00_

Date: Wed 19.3.25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	S	10 Mar '25								17 Mar '25			
										M	T	W	T	F	S	S	M	T	W	T	F
30			MakeFile	3 days	Tue 22.4.25	Thu 24.4.25	13	Lukáš Úradník													
31			Installer/uninstall	5 days	Mon 7.4.25	Fri 11.4.25	18	Roman Láncoš													
32			Záver	5 days	Fri 25.4.25	Thu 1.5.25	25														
33			Kontrola splnených cieľov					Katarína Kužmová													
34			Prichystanie súborov na odovzdanie				33	Katarína Kužmová; Lukáš Úradník													
35			Skúška odovzdaného riešenia				34	Lukáš Úradník; Roman Láncoš													
36			Opravy potencialnych chyb v odovzdanom riešení				35														
37			Individuálne zhrnutie cieľov				36	Katarína Kužmová; Lukáš													

Project: xuradnl00_xkuzmok00_
Date: Wed 19.3.25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone















Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only















External Tasks

External Milestone

Deadline

Progress

Manual Progress















Project: xuradnl00_xkuzmok00_ Date: Wed 19.3.25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

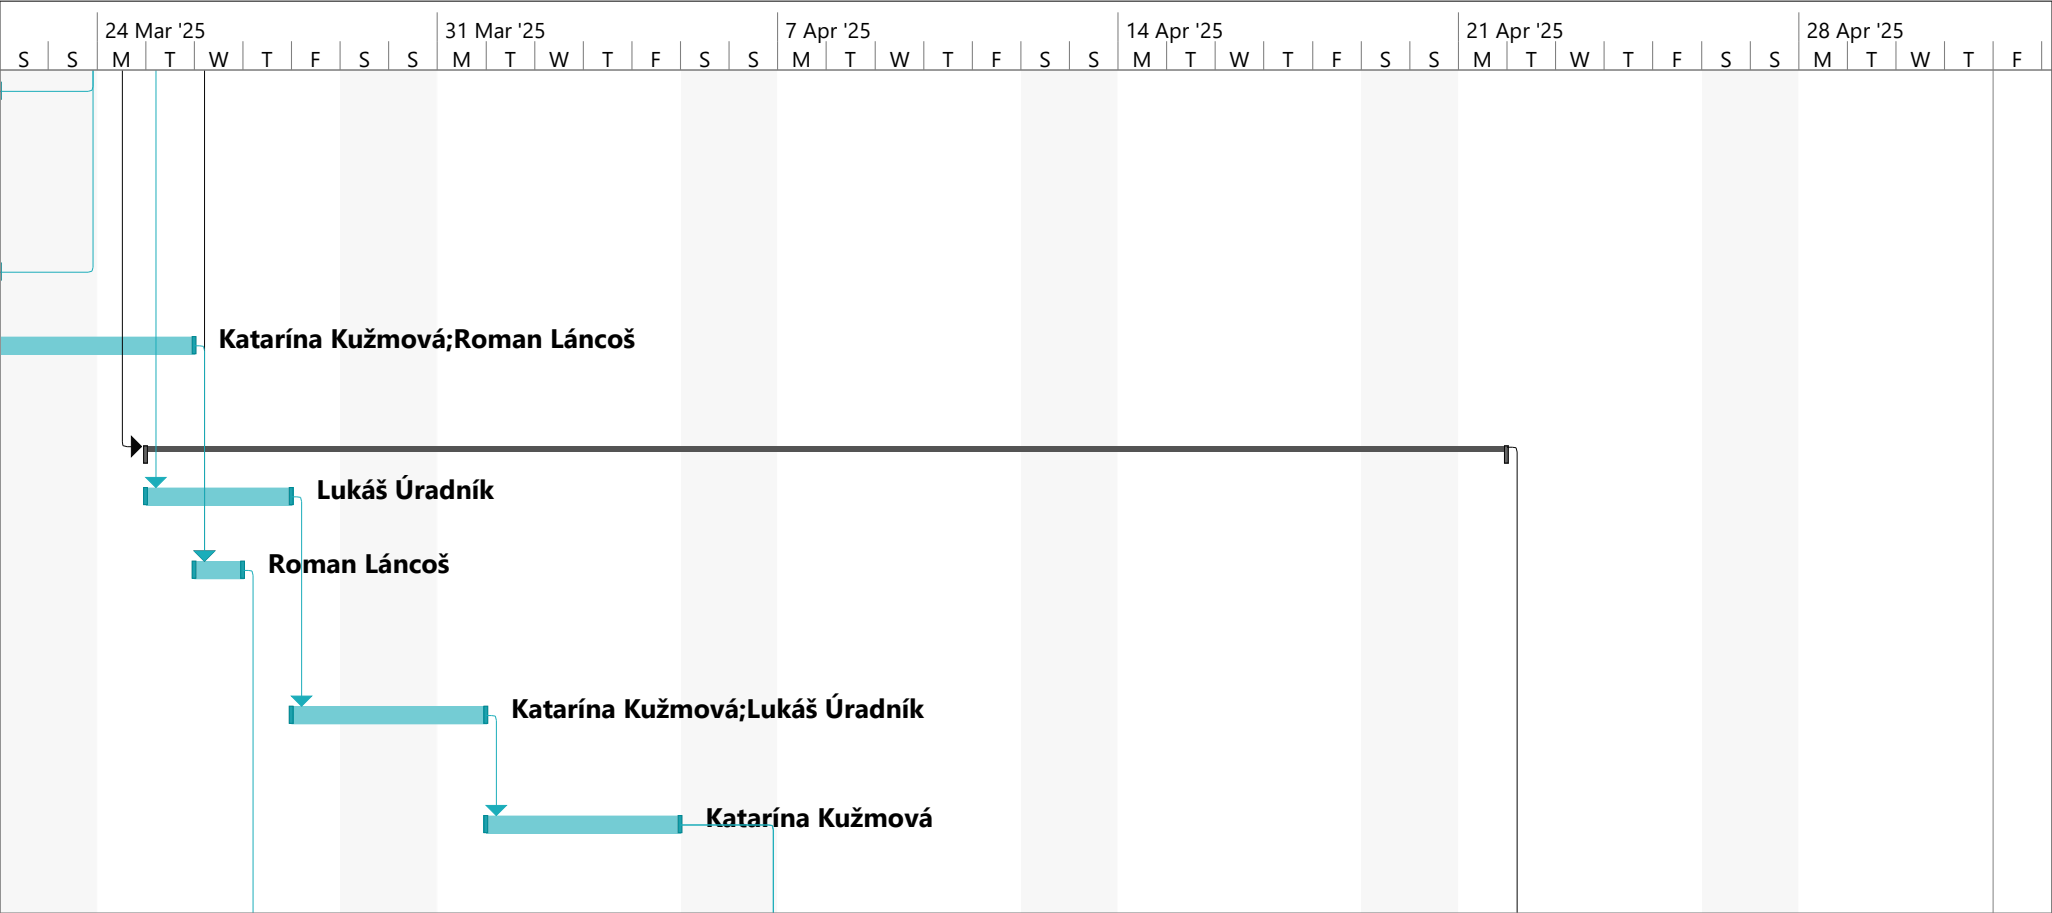

Project: xuradnl00_xkuzmok00_ Date: Wed 19.3.25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

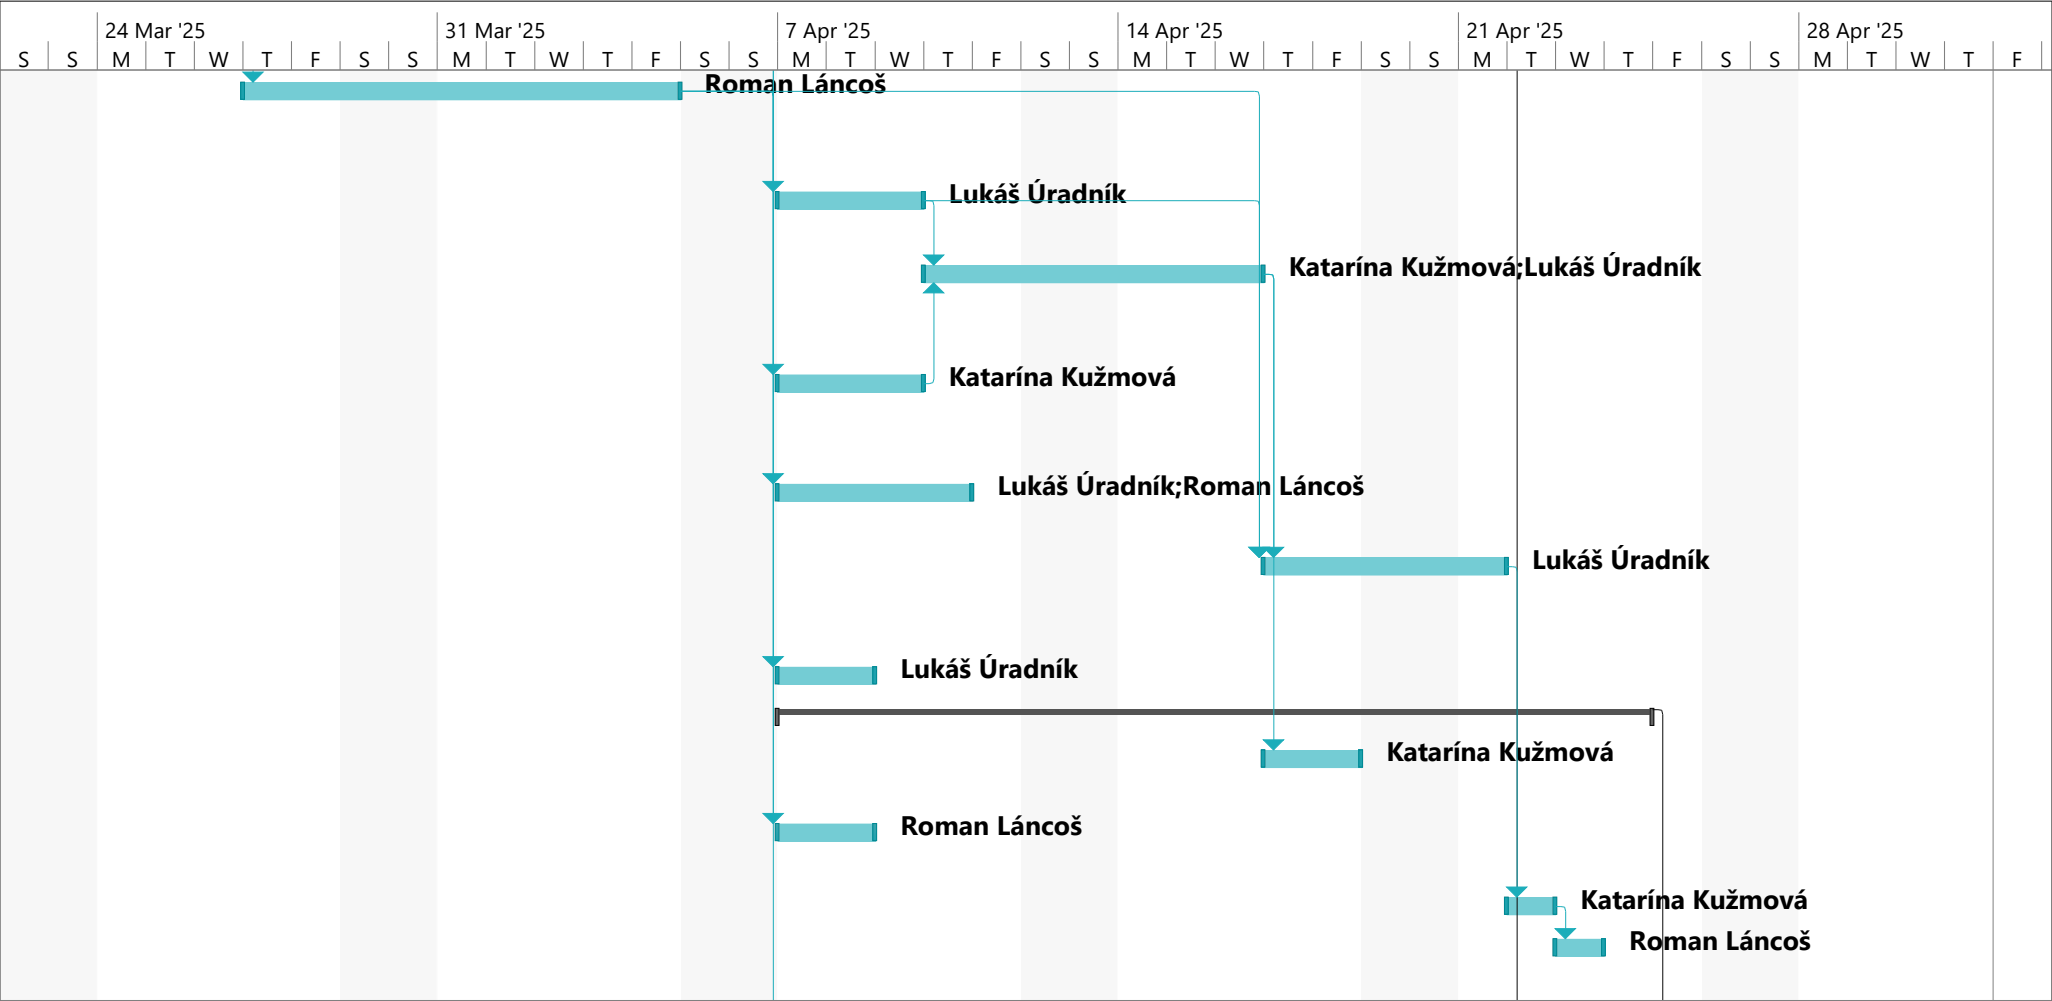

Project: xuradnl00_xkuzmok00_ Date: Wed 19.3.25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

